



KSINC WEEKLY PROGRESSREPORT



Kerala Shipping and Inland Navigation Corporation Ltd

(A Government of Kerala Undertaking)

An ISO 9001:2015 Company

CONSTRUCTION OF FERRY TERMINAL JETTY



Name of contractor	: IBMK
Agreement date	: 30-06-2021
Agreed Amount	:Rs.4,62,98,477.04
Site Handover date	: 09-07-2021
Project duration	: 18 months
Scheduled Date of Completion	: 03-05-2021
Expected Date of completion	: 08-01-2023

Scheduled progress as on 19-10-2021 2%

Achieved progress as on 19-10-2021 - 1 %

Last week progress in %

Current week progress -1 %

Current Bill Status :

Current Financial Progress : %


Images of works done at Site

Status of Work in terms of components:

- Demolition of old jetty
- Mobilization of Pontoons for work.



CONSTRUCTION OF 500 MT BULK BARGES

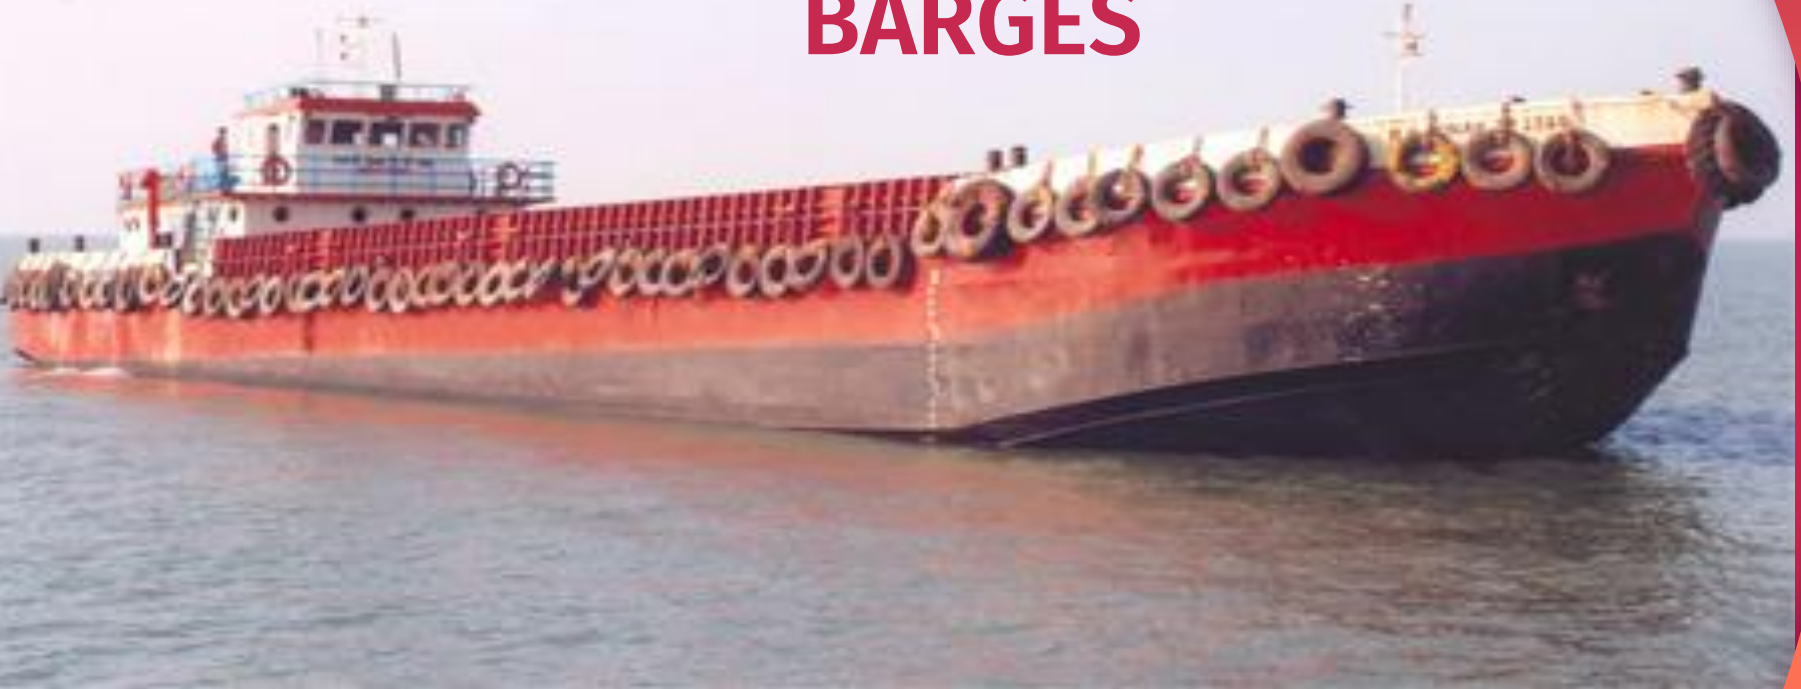

Name of contractor	:
Agreement date	:
Agreed Amount	:
Site Handover date	
Project duration	
Scheduled Date of Completion	
Expected Date of completion	:

Scheduled progress as on 19-10-2021%	
Achieved progress as on 19-10-2021 - %	
Last week progress in %	Current week progress - %
Current Bill Status :	

Current Financial Progress :%

Images of works done at Site

Status of Work in terms of components:
Preparation of estimation under process.

MODERNIZATION OF SLIPWAY

Name of contractor	:
Agreement date	:
Agreed Amount	:
Site Handover date	:
Project duration	:
Scheduled Date of Completion	:
Expected Date of completion	:

Scheduled progress as on 19-10-2021%	
Achieved progress as on 19-10-2021 - %	
Last week progress in %	Current week progress - %
Current Bill Status :	

Current Financial Progress :%

Images of works done at Site

Status of Work in terms of components:
Structural engineer submitted the design drawings
